



Cadia East Production Weekly Plan 31-Jul to 06-Aug 2025

Newmont


WK 31

	Thu, 31 July 2025				Fri, 1 August 2025				Sat, 2 August 2025				Sun, 3 August 2025				Mon, 4 August 2025				Tue, 5 August 2025				Wed, 6 August 2025					
	Day A Crew		Night B Crew		Day A Crew		Night B Crew		Day A Crew		Night B Crew		Day A Crew		Night B Crew		Day A Crew		Night B Crew		Day A Crew		Night B Crew							
CV3033	Tonnes		53,532		43,718		53,609		43,965		53,609		45,803		51,994		46,499		52,413		45,503		53,609		48,600		52,488		46,909	
	Tonnes (day)		97,251				97,574				99,412				98,493				97,916				102,209				99,397			
	Sum Tonnes		97,251				194,824				294,236				392,729				490,645				592,853				692,250			
	RMP Tonnes		102,485				194,550				296,452				396,568				493,926				590,959				688,225			
	PC1 & PC2 Tonnes		90,066				83,903				85,225				87,932				87,932				87,392				87,932			
PC2-3	Min / Max Rate		299 / 1500				580 / 1500				588 / 1500				513 / 1500				502 / 1500				624 / 1500				499 / 1500			
	Tonnes		2,630		2,630		5,762		4,444		4,825		5,512		2,813		6,208		2,462		6,367		3,813		7,154		3,307		5,463	
	PROD Tonnes (day)		5,260				4,906				5,574				7,121				7,048				9,067				8,770			
	DEVT Tonnes (day)		0				5,300				4,763				1,900				1,781				1,900				0			
	Tonnes (day)		5,260				10,206				10,337				9,021				8,829				10,967				8,770			
	RMP Tonnes		11,500				7,213				11,130				11,655				9,282				6,262				7,649			
PC2E	PC2E Ratio		51.1%		51.1%		46.1%		46.1%		46.1%		46.1%		46.1%		46.1%		46.1%		46.1%		46.1%		46.1%		46.1%		46.1%	
	Tonnes		21,005		21,005		16,418		18,048		16,800		18,048		18,048		18,048		18,048		18,048		17,799		18,048		18,048		18,048	
	PROD Tonnes (day)		42,009				34,467				34,848				36,096				36,096				35,847				36,096			
	RMP Tonnes		41,593				35,739				35,739				35,739				35,739				35,739				35,739			
PC2W	PC2W Ratio		48.9%		48.9%		53.9%		53.9%		53.9%		53.9%		53.9%		53.9%		53.9%		53.9%		53.9%		53.9%		53.9%		53.9%	
	Tonnes		20,084		20,084		19,184		21,088		19,629		21,088		21,088		21,088		21,088		21,088		20,797		21,088		21,088		21,088	
	PROD Tonnes (day)		40,167				40,271				40,717				42,176				42,176				41,885				42,176			
	RMP Tonnes		39,770				41,758				41,758				41,758				41,758				41,758				41,758			
PC1	Min / Max Rate		950 / 750		750 / 750		750 / 750		1196 / 750		750 / 750		973 / 750		750 / 750		1047 / 750		750 / 750		1084 / 750		1084 / 750		750 / 750		973 / 750		750 / 750	
	PROD Tonnes (shift)		7,889		0		9,164		0		9,660		0		9,660		0		9,660		0		9,660		0		9,660		0	
	PROD Tonnes (day)		7,889				9,164				9,660				9,660				9,660				9,660				9,660			
	PC1 Ore pass tonnes (shift)		1,925		0		3,080		385		2,695		1,155		385		1,155		1,155		0		1,540		2,310		385		2,310	
	PC1 Ore pass tonnes (day)		1,925				3,465				3,850				1,540				1,155				3,850				2,695			
	Total Tonnes		9,814				12,629				13,510				11,200				10,815				13,510				12,355			
	PC1 RMP Tonnes		7,697				3,890				9,424				9,424				9,424				9,424				9,424			
	PC1 Ore pass RMP Tonnes		2,337				5,534				2,128				1,293				1,282				1,948				2,715			
****For system manager settings, refer to Cadia East COB Feeder Strategy TARP, please adjust the system manager deadband setting as per weekly plan daily if FISEZ date changes****																														
PC2-3 Tasks	Thu, 31 July 2025				Fri, 1 August 2025				Sat, 2 August 2025				Sun, 3 August 2025				Mon, 4 August 2025				Tue, 5 August 2025				Wed, 6 August 2025					
	Day		Night		Day		Night		Day		Night		Day		Night		Day		Night		Day		Night		Day		Night			
Associated level Tasks and Interactions	FISEZ #189				FISEZ #189																									
	Hot Seat		Hot Seat		Hot Seat		Hot Seat		Hot Seat		Hot Seat		Hot Seat		Hot Seat		Hot Seat		Hot Seat		Hot Seat		Hot Seat		Hot Seat		Hot Seat		Hot Seat	
	EXT2324 Roadwork																													
	Transport panels down to PC23 using Haul Truck 21																													
Development Interactions (4425 Level - PC23)																														
PC2 Tasks	Thu, 31 July 2025				Fri, 1 August 2025				Sat, 2 August 2025				Sun, 3 August 2025				Mon, 4 August 2025				Tue, 5 August 2025				Wed, 6 August 2025					
	Day		Night		Day		Night		Day		Night		Day		Night		Day		Night		Day		Night		Day		Night			
Associated level Tasks and Interactions	No Sandvik to be used in PC2 (Except for prep tonnes and during FISEZ)																													
					Job 03 Zone Validations										Job 10 VIMS Onboard Addressing						Job 12 Geotech Inspection / Scan				Job 13 Road Scan					
	Job 01 EXT204 Continuous Intersection Pour				Job 04 EXT204 Roadwork- Lay, Infill & Grout Panels																									
					Job 05 PC2E MIA Inspection																Job 11 Bog 4410 East Collection Stockpile									
	214 / 204 VOD Door Repairs				East Collection Belt Ore Sampling												PC2W Dust Extract Comp. Service				PC2W Dust Extract Comp. Service									
Development Interaction & Request (4455 Level - PC2)					Sandvik Hut Removal						Job 06 EXT206 / 218 FRS Opportune																			
							VR80 Main Decline Blockage																							
On-going Tasks	Ore samples per shift to be taken (Ensure to fill-in the sampling table attached)																													
PC1 Tasks	Thu, 31 July 2025				Fri, 1 August 2025				Sat, 2 August 2025				Sun, 3 August 2025				Mon, 4 August 2025				Tue, 5 August 2025				Wed, 6 August 2025					
	Day		Night		Day		Night		Day		Night		Day		Night		Day		Night		Day		Night		Day		Night			
Associated level Tasks and Interactions			Ore Pass Bogging Only				Ore Pass Bogging Only				Ore Pass Bogging Only				Ore Pass Bogging Only				Ore Pass Bogging Only				Ore Pass Bogging Only				Ore Pass Bogging Only			
											Job 07 PC1W MIA Inspection						4670 WKS Fire System Inspection								PC1 Dust Extract Comp. Service					
					Job 02 Atmosphere Monitoring						Job 08 PC1E MIA Inspection						Job 09 EXT116 Route Recording													
Development Interaction & Request (PC1-2 Development)							VR80 Main Decline Blockage																							
On-going Tasks	Ore samples per shift to be taken (Ensure to fill-in the sampling table attached)																													
Other Tasks	Thu, 31 July 2025				Fri, 1 August 2025				Sat, 2 August 2025				Sun, 3 August 2025				Mon, 4 August 2025				Tue, 5 August 2025				Wed, 6 August 2025					
	Day		Night		Day		Night		Day		Night		Day		Night		Day		Night		Day		Night		Day		Night			
☐ Manage Decline Sump	2m / day advance				2m / day advance				2m / day advance				2m / day advance				2m / day advance				2m / day advance				2m / day advance					
☐ VR101/SP32 Pumping																														
☐ Civil Infra Maint.	4h				4h				4h				4h				4h				4h				4h					
☐ FRS (m3)																														
☐ Concrete (m3)			40				8								8								8							
☐ Grout (m3)											12								12				8				6			
Concrete Priority: 1) PC1-2 Structural Pours 2) PC2-3 Roadworks 3) PC2 Roadworks 4) PC1																														
☐ Maxi Spray Rig 1	Production		Production		Production		Production		Production		Production		Production		Production		Production		Production		Production		Production		Production		Production			
☐ Maxi Spray Rig 2	Production		Production		Production		Production		Production		Production		Production		Production		Production		Production		Production		Production		Production		Production			
☐ Single Boom Rig	Production		Production		Production		Production		Production		Production		Production		Production		Production		Production		Production		Production		Production		Production			
☐ Jumbo Rig	Production		Production		Production		Production		Production		Production		Production		Production		Production		Production		Production		Production		Production		Production			

	Weekly Tasks							LEGEND	MIA	Development	Electrical	Geotech	Projects	
	Job Number	Date	Shift	Task Name	Specific Working / Interaction Area	Pre-work Required	Description		Production	Resource Request	Fixed Plant Maint	Opportune	Fleet	
☐	PC2-3 DEVT Interaction	Thu, 31/07/2025	DS	Transport Panels down to PC23	PC23	-	Transport panels down to PC23 using Haul Truck 21 for EXT-2324 road work							
☐	PC2-3 DEVT Interaction	Thu, 31/07/2025	DS	EXT2324 Roadwork	PC23	-	PC2-3 EXT2324 Roadwork							
☐	1	Thu, 31/07/2025	DS	EXT204 Continuous Intersection Pour	EXT204	-	EXT-204 intersection roadwork continuous pour (48m3) required to enable access into EXT-202. EXT-204 panel laying won't commence until intersection pour is complete.							
☐	FPM Interaction	Thu, 31/07/2025	DS	EXT214 / EXT204 VOD Door Repairs	PC2	-	FPM will be repairing grease lines on VOD doors at PC2. Ensure 204 door repairs are not concurrent with continuous concrete pour for 204 intersection.							
	Prod. Civil Interaction	Fri, 1/08/2025	DS	Sandvik Hut Removal	PC2 Breakdown Bay	-	Remove Sandvik Hut from 4455 Breakdown Bay and relocate to behind the Ridgeway change house. Tarp and seal hut from weather.							
☐	2	Fri, 1/08/2025	DS	PC1 Atmosphere Monitoring	PC1 (any 2 drives) Must not be red TARP (i.e. must be accessible on foot)	-	Pause loader operations in up to two drives for 30 minutes to install atmosphere monitoring devices on the backs and leave the area. Resume loader operations as normal and run for 4 hours non-stop. Return to the area to retrieve the devices and leave the area.							
☐	3	Fri, 1/08/2025	DS	PC2 Automation Zone Validations	PC2 Zone 1, 2 & 3	-	Demarcations in other zones while working in zones for barrier validation. 2x operators required to act as sentries for Zone 1, 1x operator required as sentry for zone 2 and 3.							
☐	4	Fri, 1/08/2025	DS	EXT204 South Roadwork - Lay, Infill & Grout Panels	EXT204 South	-	1. Laying Panel (30m per section) 2. Grout Panel (30m per section) 3. Infill Concrete (30m per section) 8m3/24hrs of concrete required for infills. 12m3/24hrs of grout required.							
☐	5	Fri, 1/08/2025	DS	MIA PC2E Inspection (Zone1 / 2 / 3)	PC2 Zone 1 & 2 & 3	-	MIA Inspection on PC2E Automation Inspection - (2h) Will require east zone outage. Production to use this time for drive sump maintenance.							
☐	FPM Interaction	Fri, 1/08/2025	DS	East Collection Belt Ore Sampling	PC2E	-	Sample collection at CV022 collection belt for 1 hour.							
☐	PC2-3 DEVT Interaction	Sat, 2/08/2025	DS	VR80 Main Decline Blockage	SP15	-	Main Decline Blockage for approximately 6 hours (SP9 to Leg 4) . Relocation of 11kv power cable required to create loading pocket.							
☐	6	Sat, 2/08/2025	NS	EXT206 / EXT218 FRS Opportune	PC2	-	EXT206 W8 & E2 require FRS encapsulation following geotech inspections. EXT218 E11 brow beam needs to be lowered. 206 rehab priority over 218.							
☐	7	Sat, 2/08/2025	NS	MIA PC1W Inspection	PC1W (North / South Zone)	-	Routine MIA Inspection, Outage on West, production to use this time for drive sump maintenance.							
☐	8	Sat, 2/08/2025	NS	MIA PC1E Inspection	PC1E (North / South Zone)	-	Routine MIA Inspection, Outage on East, production to use this time for drive sump maintenance.							
☐	9	Mon, 4/08/2025	DS	Route Recording - EXT116 with LD210 Monday (DS)	PC1 EXT116	-	EXT116 with LD210 during D/S route recording after Epiroc Barrier update							
☐	10	Mon, 4/08/2025	DS	VIMS Onboard Addressing	PC2	-	WesTrac employee will be on level with Troy Arrow to complete VIMS health monitoring job on loaders.							
☐	FPM Interaction	Mon, 4/08/2025	DS	PC2W Dust Extraction Compressor Service	PC2W	-	CE PC2W Area Dust Extraction Compressor Service 12Hrs. Should be no impact underground unless there is a breakdown on another compressor.							
☐	FPM Interaction	Mon, 4/08/2025	DS	4670 Workshop Fire System Inspection	PC1	-	Fire Deluge System Inspection PC1 4670 Workshop 2Hrs.							
☐	11	Tue, 5/08/2025	DS	Bog 4410 East Collection Stockpile	4410 East Collection	Scope out amount of material to be bogged. Tram LD056 from TC Drive down to 4410.	Fixed Plant require access to 4410 East Collection stockpile (behind the vent doors). Material needs to be bogged out before they can access. LD056 will likely have to be used - contact John Jones for exact location.							
☐	FPM Interaction	Tue, 5/08/2025	DS	PC2E Dust Extraction Compressor Service	PC2E	-	CE PC2E Area Dust Extraction Compressor Service 12Hrs. Should be no impact underground unless there is a breakdown on another compressor.							
☐	12	Tue, 5/08/2025	DS	EXT228 / EXT224 Fragmentation Scan	EXT228 / EXT224	Drive Bunding required	Inspection / LIDAR Scan / Damage Mapping							
☐	FPM Interaction	Wed, 6/08/2025	DS	PC1 Dust Extraction Compressor Service	PC1	-	CE PC1 FI3033-CP Compressor Service 6Hrs. Should be no impact underground unless there is a breakdown on another compressor.							
☐	13	Wed, 6/08/2025	DS	Road Scan	PC2	-	Peter Naylor will be underground at PC2 to continue the road scan program. LV will be driving up and down in the drive with a scanner mounted on the front. TARGET = 4 drives							
RECURRING TASKS														
☐	Priority 1	Week 29	DS	SP32 Campaign	SP32	-	Bog sump to maintain access to return airway							
☐	Priority 2	Week 29	DS	VR4 Sump clearing / bogging	VR4 Sump	-	Bog sump for VR4 (date is flexible, ensure to contact FPM Supervisor prior to bogging the sump)							
☐	Priority 3	Week 29	DS	PC1 / PC2 / PC23 Ore Sampling	PC1	-	2 ore sample to be taken per shift - Priority on sampling requirement as per page 1. Ensure the sampling table, showed in the sampling page is filled out, scanned and emailed to PC1 supervisor in charge. Continue to sample EXT112-W-08 / EXT 112-W-07 every 1,500t.							

CIVIL ACTIVITIES AND PROJECTS					WK 31													
					Thu, 31 Jul		Fri, 1 Aug		Sat, 2 Aug		Sun, 3 Aug		Mon, 4 Aug		Tue, 5 Aug		Wed, 6 Aug	
Priority	Location	Task Description	Resources	Responsible	Day	Night	Day	Night	Day	Night	Day	Night	Day	Night	Day	Night	Day	Night
Mining and Civil Works																		
	PC2	PC2 VOD maintenance - as per VOD audit																
	PC1	PC1 VOD maintenance - as per VOD audit																
	TC Drive	Fabricate shutters for wall moulds & transport stillage			10												10	
	TC Drive	Fabricate additional bumper moulds					10											10
	HV Slab	Install Tie down plates for stands				10												
	PC2	Remove Sandvik hut, relocate to RWY behind change house (Tarp and seal from weather)					10											
1	Big House	Locker modifications - move installed lockers, move exisiting back to original position							10	10	10	10	10	10	10	10		
Opportune / Upcoming																		
	Decline	Campagne Victaulic line spb111 - 114, Install thrust brackets, raise line, L pins, Remove extension pipes (Ongoing)																
	VI-0786, MA278	Once MA278 (refuge chamber) is repaired Relocate MA278 (refuge chamber) from Surface to 4750-SPB-128																
	VI-0786, MA2250	Once MA278 (refuge chamber) is relocated to 4750-SPB-128 Relocate MA2250 (refuge chamber) from 4750-SPB-128 to Surface																
	VI-0884	PC2 Workshop vent upgrade (VAF212 GSM to be completed prior)																
	VI-0818	Install 55kw Fan @ SPB139 workshop Remove the exisiting duct into the lower half of workshop and install new 1400mm duct. Ensure the duct includes Lobsterback / radius pieces and a cross piece.																
	Bus bay to Tyre bay	Turn Bus bay into tyre bay. Dismantle store., Chem bay move, Toilet relocation, Refuge chamber relocation, Lockers to cribroom (Awaiting on 202N Sump SW breakthrough and Tagboard installation)																
	TC Drive	Grout bowl modifications & repairs																
	TC Drive	Fabricate and install storage cage & bottle rack on pump truck																
Panel Shed & Logistics																		
	Panel Shed	A+ panels (poured / flipped)	49	7 / Day	7		7		7		7		7		7		7	
	Panel Shed	B panels (poured / flipped)	DO NOT POUR	1 / Day														
	Panel Shed	F panels (poured / flipped)	7	1 / Day	1		1		1		1		1		1		1	
	Panel Shed	G panels (poured / flipped)	7	1 / Day	1		1		1		1		1		1		1	
	Panel Shed	H panels (poured / flipped)	14	2 / Day	2		2		2		2		2		2		2	
	Panel Shed	K panels (poured / flipped)	DO NOT POUR	4 / Day														
	Panel Shed	W panels (poured / flipped)	DO NOT POUR															
	Panel Shed	Cobble Stone (A+Panel size)	DO NOT POUR															
	Panel Shed	Wall Panels (40MPA w/ Firbres)	28	4 / Day	4		4		4		4		4		4		4	
	Panel Shed	Bumpers (40MPA w/ Firbres)	28	4 / Day	4		4		4		4		4		4		4	
	Panel Shed	Sign Blocks with posts (Dual pole Rectangular Bases, 2,000x1,000x400)	DO NOT POUR	1 / Day														
	Panel Shed	Sign Blocks with posts (Square Bases, 1,000x1,000x400)	DO NOT POUR	4 / Day														
	Panel Shed	Chevron	DO NOT POUR															
	Panel Shed	1m3 Block	DO NOT POUR	1 / Day														
	Panel Shed	Jersey barrier	DO NOT POUR	4 / Day														
	Surface	Transfer Panels to Cadia East Portal, CEP (On-going)	112	16 / Shift														
	PC2	Deliver & Maintain SA-160	3000L	At least 1 per Swing									10					
	PC2-3	Transport Road panels					10		10		10				10		10	
	PC2-3	Transport 2x Keech's excavators & implements			10													
Cleaners																		
		Publish Refuge Chamber Audit - Circulate Across Site & Archive in Sharepoint			2		1		1		1		1		1		1	
		Cribroom (11) /Admin /Toilet (69) Maintenance			5		5		5		5		5		5		5	
		Refuge Chamber & FABs Audits (6) / Maintenance - CE, RWY & VENT ADDIT x 55			2		4		4		4		4		4		4	
		Weekly SAP Order for Consumables			1													

PC2 Activities

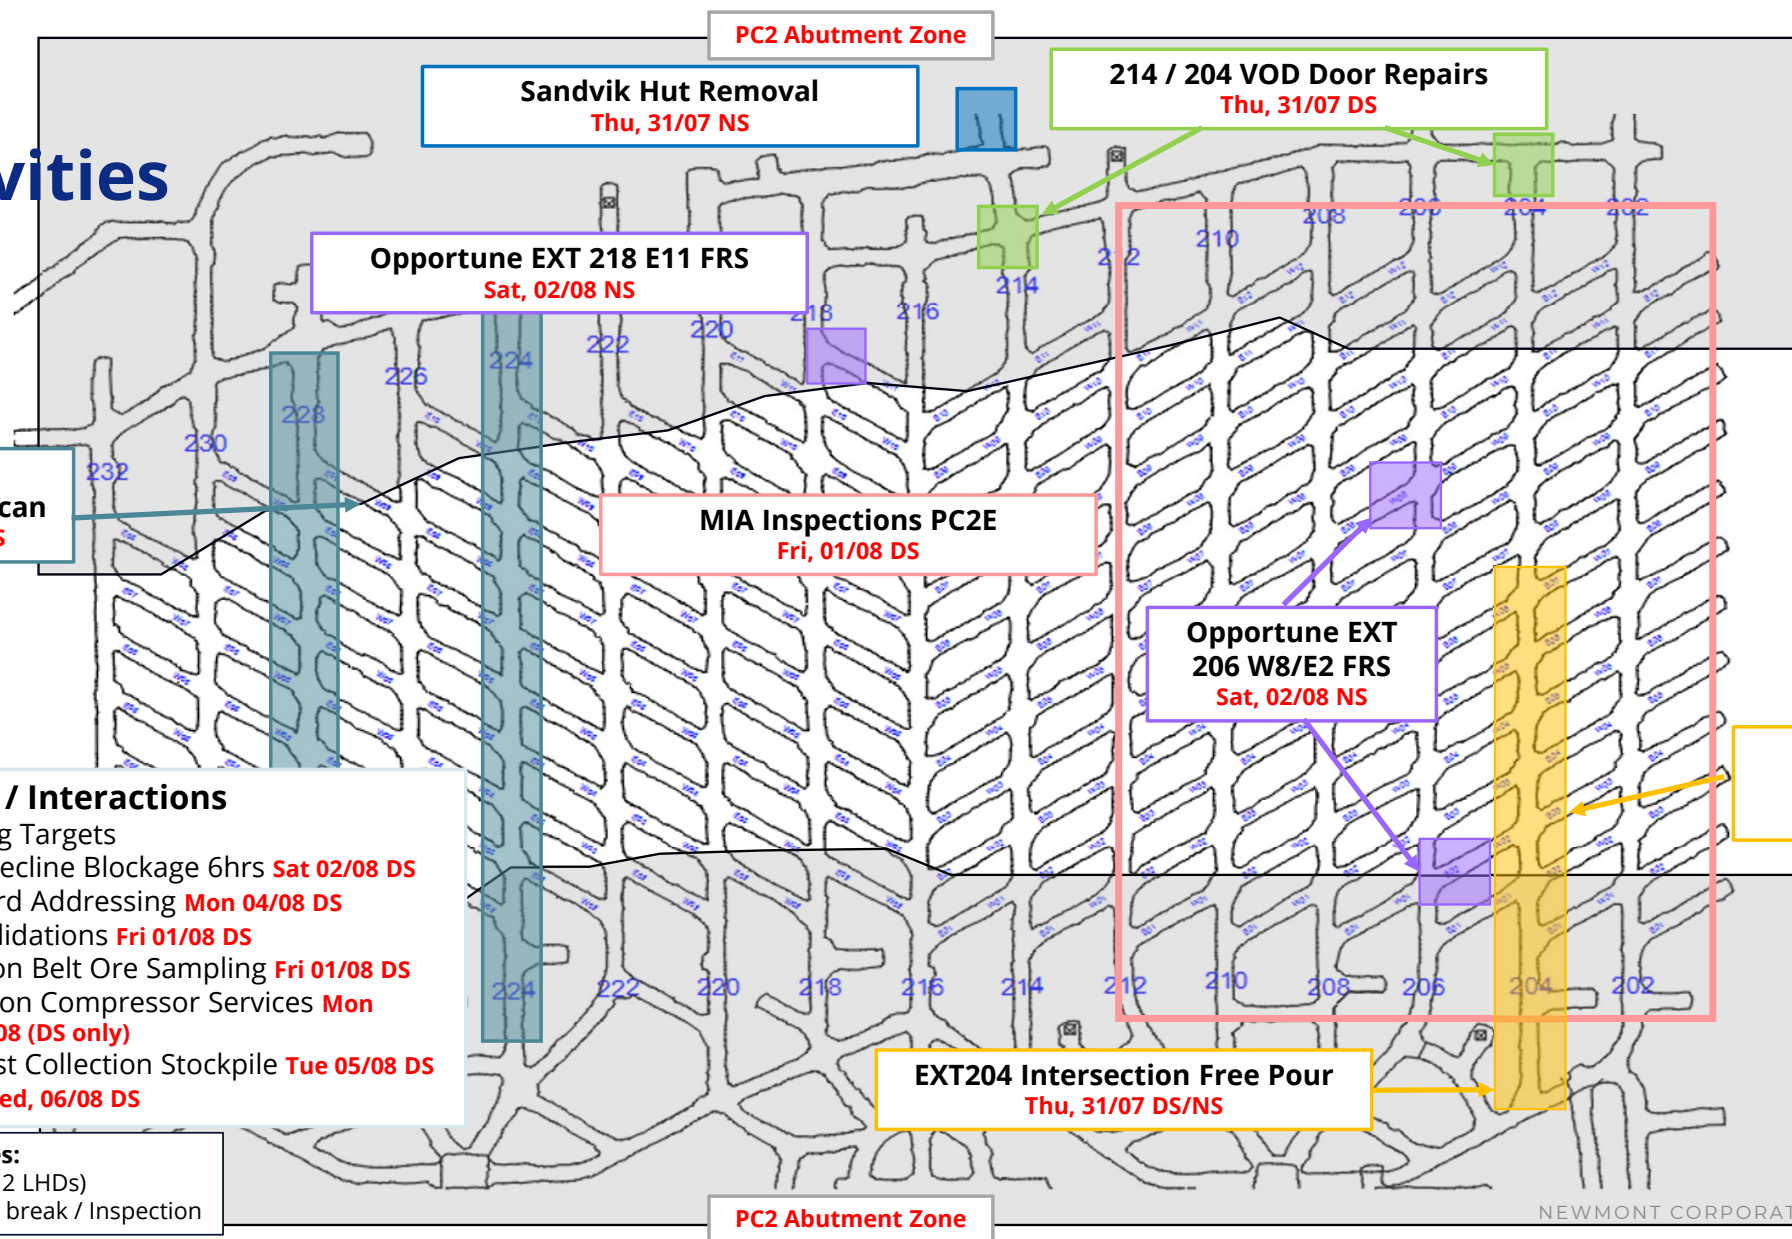


Other Tasks / Interactions

- PC2 Sampling Targets
- VR80 Main Decline Blockage 6hrs **Sat 02/08 DS**
- VIMS Onboard Addressing **Mon 04/08 DS**
- MIA Zone Validations **Fri 01/08 DS**
- East Collection Belt Ore Sampling **Fri 01/08 DS**
- Dust Extraction Compressor Services **Mon 04/08, Tue 05/08 (DS only)**
- Bog 4410 East Collection Stockpile **Tue 05/08 DS**
- Road Scan **Wed, 06/08 DS**

Normal Activities:

- 12 EXT bogging (12 LHDs)
- 2 EXT secondary break / Inspection

PC1 Activities

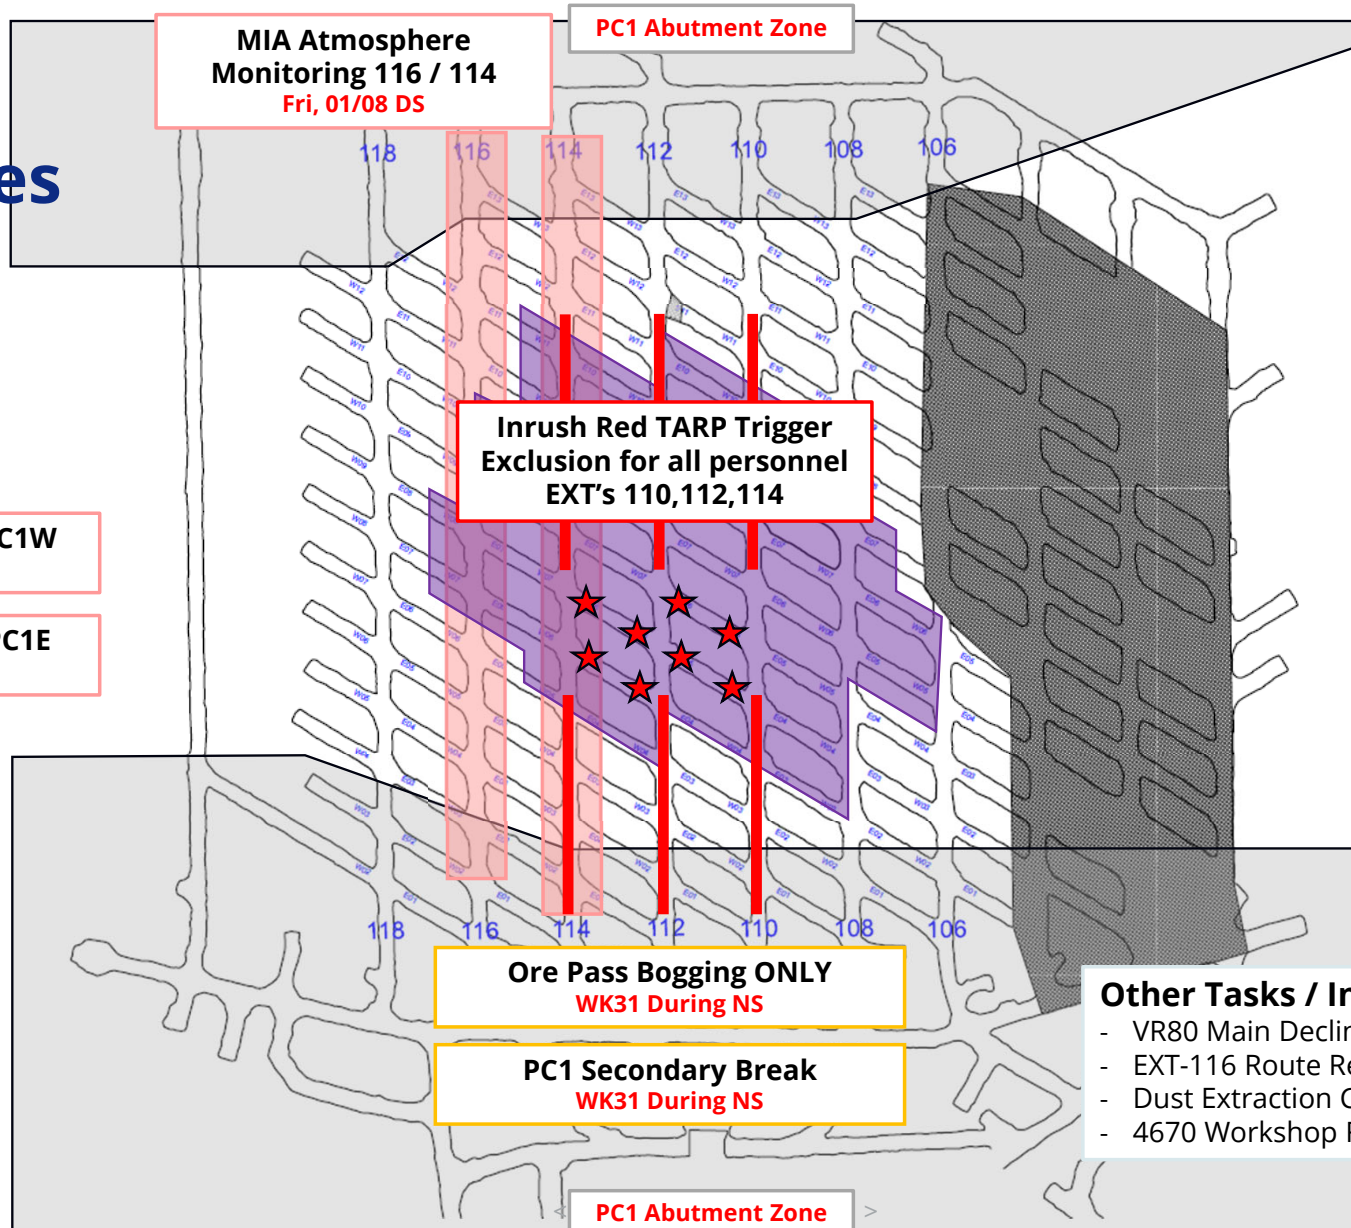


- Other Tasks / Interactions**
- VR80 Main Decline Blockage 6hrs **Sat 02/08 DS**
 - EXT-116 Route Recording **Mon 04/08 DS**
 - Dust Extraction Compressor Service **Wed 06/08 DS**
 - 4670 Workshop Fire System Inspection **Mon 04/08 DS**

PC2-3 Activities

EXT2324 Roadwork
WK31

Deliver Panels down to PC23
using Haul Truck 21
WK31

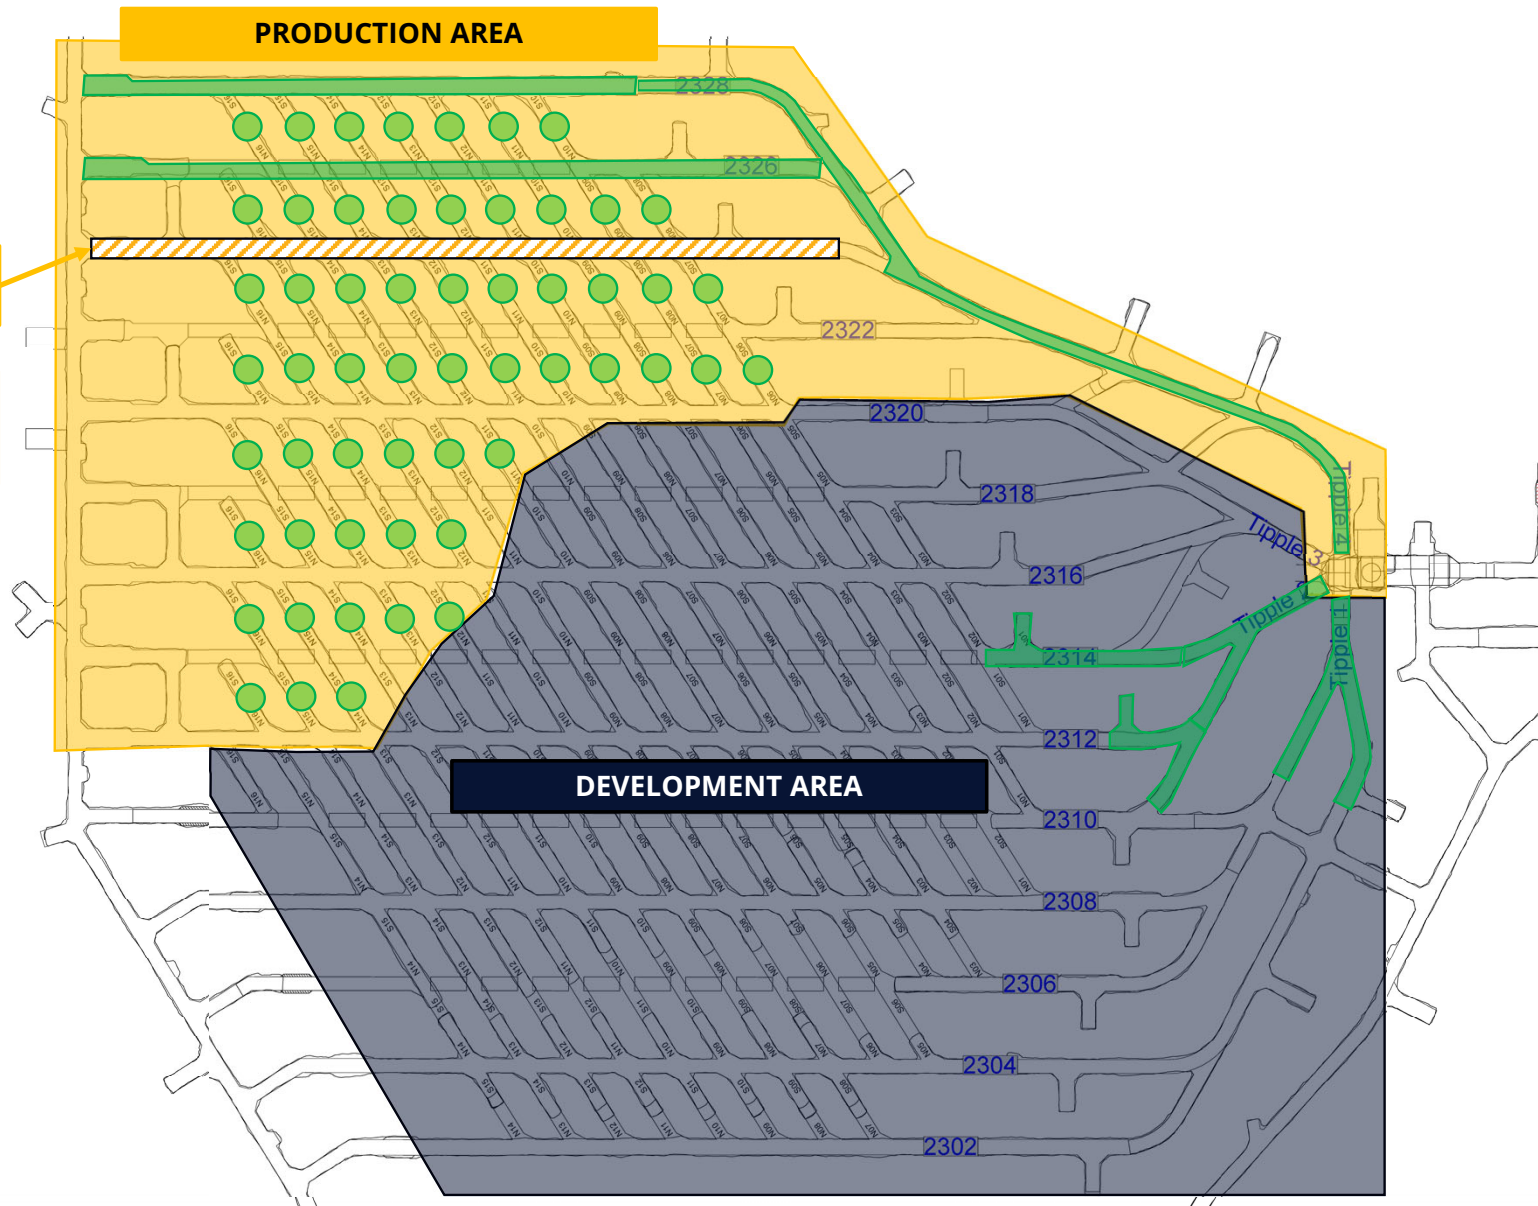

WK 31															
		Thu, 31 Jul 2025		Fri, 1 Aug 2025		Sat, 2 Aug 2025		Sun, 3 Aug 2025		Mon, 4 Aug 2025		Tue, 5 Aug 2025		Wed, 6 Aug 2025	
Offsite	UG Service	Day	Night	Day	Night	Day	Night	Day	Night	Day	Night	Day	Night	Day	Night
Surface Workshop	Lent out	A Crew	B Crew	A Crew	B Crew	A Crew	B Crew	A Crew	B Crew	A Crew	B Crew	A Crew	B Crew	A Crew	B Crew
Fleet Maintenance															
	Golden Rules:														
PC2	Daily Service Schedule														
LD115 (Priority 2)	8:05 AM														
LD140 (Priority 11)	8:55 AM									12	12				
LD131 (Priority 10)	10:15 AM														
LD141 (Priority 12)	11:05 AM														
LD120 (Priority 3)	11:55 AM														
LD121 (Priority 4)	12:45 PM														
LD143 (Priority 14)	2:05 PM														
LD125 (Priority 7)	2:55 PM														
LD129 (Priority 8)	8:05 PM														
LD144 (Priority 15)	8:55 PM														
LD145 (Priority 16)	10:15 PM	12	12	12	12										
LD110 (Priority 1)	11:05 PM														
LD122 (Priority 5)	11:55 PM														
LD124 (Priority 6)	12:45 AM											12	12		
LD142 (Priority 13)	2:05 AM														
LD130 (Priority 9)	2:55 AM					12	12	12	12						
PC23															
LD202 (Priority 4)	8:30 AM														
LD205 (Priority 7)	9:10 AM														
LD201 (Priority 3)	9:50 AM														
LD090 (Priority 2)	11:00 AM														
LD204 (Priority 6)	11:40 AM														
LD089 (Priority 1)	12:20 PM														
LD203 (Priority 5)	1:00 PM														
LD091 (Priority 8)	2:10 PM														
LD092 (Priority 9)	2:50 PM														
LD093 (Priority 10)	3:30 PM														
PC1															
LD210 (Priority 7)	8:00 AM													12	12
LD079 (Priority 5)	9:00 AM														
LD071 (Priority 2)	10:30 AM														
LD076 (Priority 4)	12:00 PM														
LD070 (Priority 1)	2:30 PM		12	12											
LD072 (Priority 3)	8:00 PM														
LD083 (Priority 6)	9:00 PM														
Spares															
Parked up loaders															
LD078 (Priority PCR)	Offsite														
LD085 (Priority Parked Up)	Offsite														
LD086 (Priority Parked Up)	Offsite														
LD094 (Priority Parked Up)	Offsite														
LD084 (Priority PCR)	Offsite														
LD128 (Priority PCR)	Offsite														
LD123 (Priority PCR)	Offsite														
LD126 (Priority Parked Up)	Offsite														
LD127 (Priority Parked Up)	Offsite														
LD146 (Priority New)	Offsite														
LD147 (Priority New)	Offsite														
Ancillary Equipment															
LD056 - Sandvik LH517															
LD062 - Sandvik LH621															
DD011 - Rehab Jumbo															
DR010 - Single Boom								12	8						
IT012 - 120 Volvo															
RB014 - T9 Rockbreaker															
RB015 - T9 Rockbreaker	2:00 AM														
RB012 - Cat RB															
RB007 - SB Drill				12											
RB010 - SB Drill	2:00 AM														
RB013 - SB Drill															
CW001 - Water Cannon															
CW002 - Water Cannon															
XT016 - Shotcrete	2:00 AM	1													
IT021 - Low Cab												12	12		
IT025 - Low Cab															
IT020 - Low Cab															
IT024 - Low Cab	2:00 AM														
XB002 - Simba															
CB051 - Cabolter															
XB004 - Cabolter		3													
IT006		0.5													
IT009															
IT012															
IT022															
TR019	2:00 AM														
RB016															

	LIGHT VEHICLE SERVICE SCHEDULE - Y25WK31					
Column1	DATE	VEHICLE	DEPARTMENT AND OR OPERATOR	DELIVERY TIME	SERVICE TEXT	Scheduled Outage
	31-Jul			6AM		
	THURSDAY	TR447	Cadia East / Nick Fryer	6AM	PM Service Light Vehicle - 'A' FTS800	12
		LV400	Open Pit / Arvic Osorio	6AM	STA 2008 Und 8 ton GVM	12
		LV368	Cadia East / Nigel Ryan	6AM	CARRY OUT C SERVICE (8 MONTHLY)	12
		LV401	Ore treatment / Michael Swan	6AM	PM Service Light Vehicle - Import 'A'	12
				6AM		
	31-Jul			6PM		
	THURSDAY	TR252	Cadia East / Nicholas Brooking	6PM	PM Service Light Vehicle - 'Lube Service	12
		LV329	Cadia East / Johan Hough	6PM	PM Service Light Vehicle - Import 'B'	12
				6PM		
	1-Aug			6AM		
	FRIDAY	TR379	Cadia East / James Lingier	6AM	PM Service Light Vehicle - 'A'	12
		LV492	Cadia East / Nick Fryer	6AM	CARRY OUT C SERVICE (8 MONTHLY)	12
		LV391	Cadia East / Michael Evens	6AM	CARRY OUT A+SERVICE (MONTHLY)	12
				6AM		
	1-Aug			6PM		
	FRIDAY	BS312	Cadia East / Michael Evens	6PM	Carry Out Lube Service + repairs	12
		LV501	Cadia East / Nick Fryer	6PM	CARRY OUT C SERVICE (8 MONTHLY)	12
		LV358	Cadia East / Arvic Osorio	6PM	CARRY OUT A+SERVICE (MONTHLY)	12
				6PM		
	2-Aug			6AM		
	SATURDAY	LV495	Cadia East / Nick Fryer	6AM	CARRY OUT B SERVICE (4 MONTHLY)	12
		LV422	Cadia East / Michael Evens	6AM	CARRY OUT A+SERVICE (MONTHLY)	12
		LV319	Cadia East / Johan Hough	6AM	PM Service Light Vehicle - Import 'A'	12
		TR041	Emergency Response / Mick Dillon	6AM	STA 2008 Und 8 ton GVM	6
				6AM		
	2-Aug			6PM		
	SATURDAY	LV407	Cadia East / Michael Evens	6PM	CARRY OUT B SERVICE (4 MONTHLY)	12
		LV388	Cadia East / Matthew Gibbons	6PM	CARRY OUT A+SERVICE (MONTHLY)	12
		LV354	Cadia East / Nigel Ryan	6PM	CARRY OUT A+SERVICE (MONTHLY)	12
		TX012	Emergency Response / Mick Dillon	6PM	PM Service Light Vehicle - Trailer	6
				6PM		
	3-Aug			6AM		
	SUNDAY	LV371	Cadia East / Shehan Fernando	6AM	CARRY OUT A+SERVICE (MONTHLY)	12
		LV503	Cadia East / Nick Fryer	6AM	CARRY OUT A+SERVICE (MONTHLY)	12
		LV398	Cadia East / Daniel Breen	6AM	CARRY OUT A+SERVICE (MONTHLY)	12
				6AM		
	3-Aug			6PM		
	SUNDAY	LV370	Cadia East / Shehan Fernando	6PM	CARRY OUT A+SERVICE (MONTHLY)	12
		LV474	Cadia East / Michael Evens(PC1 for	6PM	CARRY OUT A+SERVICE (MONTHLY)	12
		LV509	Cadia East / Nick Fryer	6PM	CARRY OUT A+SERVICE (MONTHLY)	12
		LV513	Open Pit / Craig Miskell	6PM	Light Vehicle Repairs	6
		LV453	Cadia East / Arvic Osorio	6PM	Light Vehicle Repairs	6
		LV464	Safety / Warren Newell	6PM	Light Vehicle Repairs	6
		TR465	Supply and Logistics / Adam Shackl	6PM	Light Vehicle Repairs	6
				6PM		
	4-Aug			6AM		
	MONDAY	LV504	Cadia East / Nick Fryer	6AM	CARRY OUT A+SERVICE (MONTHLY)	12
		LV260	Cadia East / Matthew Gibbons	6AM	Light Vehicle Repairs	12
		LV330	Maintenance Dept / Shehan Fernan	6AM	Light Vehicle Repairs	6
		LV323	Cadia East / Johan Hough	6AM	Light Vehicle Repairs	12
				6AM		
	4-Aug			6PM		
	MONDAY	LV488	Cadia East / Nick Fryer	6PM	CARRY OUT B SERVICE (6 MONTHLY)	12
		LV442	Cadia East / Nigel Ryan	6PM	CARRY OUT A+SERVICE (MONTHLY)	12
		LV305	Cadia East / Johan Hough	6PM	Light Vehicle Repairs	12
		LV396	Cadia East / Arvic Osorio	6PM	Light Vehicle Repairs	6
		LV469	Asset Management / Cam Tom	6PM	Light Vehicle Repairs	6
				6PM		
	5-Aug			6AM		
	TUESDAY	LV483	Cadia East / Nick Fryer	6AM	CARRY OUT A+SERVICE (MONTHLY)	12
		LV482	Cadia East / Daniel Breen	6AM	CARRY OUT A+SERVICE (MONTHLY)	12

		LV461	Cadia East / Nigel Ryan	6AM	Light Vehicle Repairs	12
				6AM		
	5-Aug			6PM		
	TUESDAY	LV389	Cadia East / Matthew Gibbons	6PM	CARRY OUT A+SERVICE (MONTHLY)	12
		LV437	Cadia East / Nigel Ryan	6PM	CARRY OUT A+SERVICE (MONTHLY)	12
		LV088	Mining Services / Michael Evens	6PM	Light Vehicle Repairs	6
		LV225	Maintenance Dept / Jarrad Haynes	6PM	Light Vehicle Repairs	6
		LV412	Cadia East / Daniel Breen	6PM	Light Vehicle Repairs	6
				6PM		
	6-Aug			6AM		
	WEDNESDAY	LV490	Cadia East / Nick Fryer	6AM	CARRY OUT A+SERVICE (MONTHLY)	12
		LV383	Cadia East / Nigel Ryan	6AM	Light Vehicle Repairs	12
		LV214	Mining Services / Mark Mori	6AM	Light Vehicle Repairs	6
		LV212	Open pit / Amanda Delaney	6AM	Light Vehicle Repairs	6
				6AM		
	6-Aug			6PM		
	WEDNESDAY	LV512	Open Pit / Craig Miskell	6PM	CARRY OUT A+SERVICE (MONTHLY)	12
		LV294	Cadia East / Travis Small	6PM	Light Vehicle Repairs	6
		BS455	Cadia East / Andrew Bedgood	6PM	Light Vehicle Repairs	6
				6PM		

Sampling

PC1 Sampling Priorities		PC2 Sampling Priorities		PC2-3 Sampling Priorities	
Priority	Drawpoint	Priority	Drawpoint	Priority	Drawpoint
1	110W06	1	216E01	1	2322N12
2	116W12	2	214W05	2	2322S14
3	112W07	3	222E05	3	2322S15
4	114E05	4	220E05	4	2320S11
5	110E05	5	212E03	5	2320S08
6	116W05	6	226E10	6	2316S15
7	116W11	7	224E06	7	2314N13
8	110W09	8	206E02	8	2326N13
9	110W04	9	230E02	9	2326N15
10	114W10	10	222W04	10	2312N13

[illegible]
